









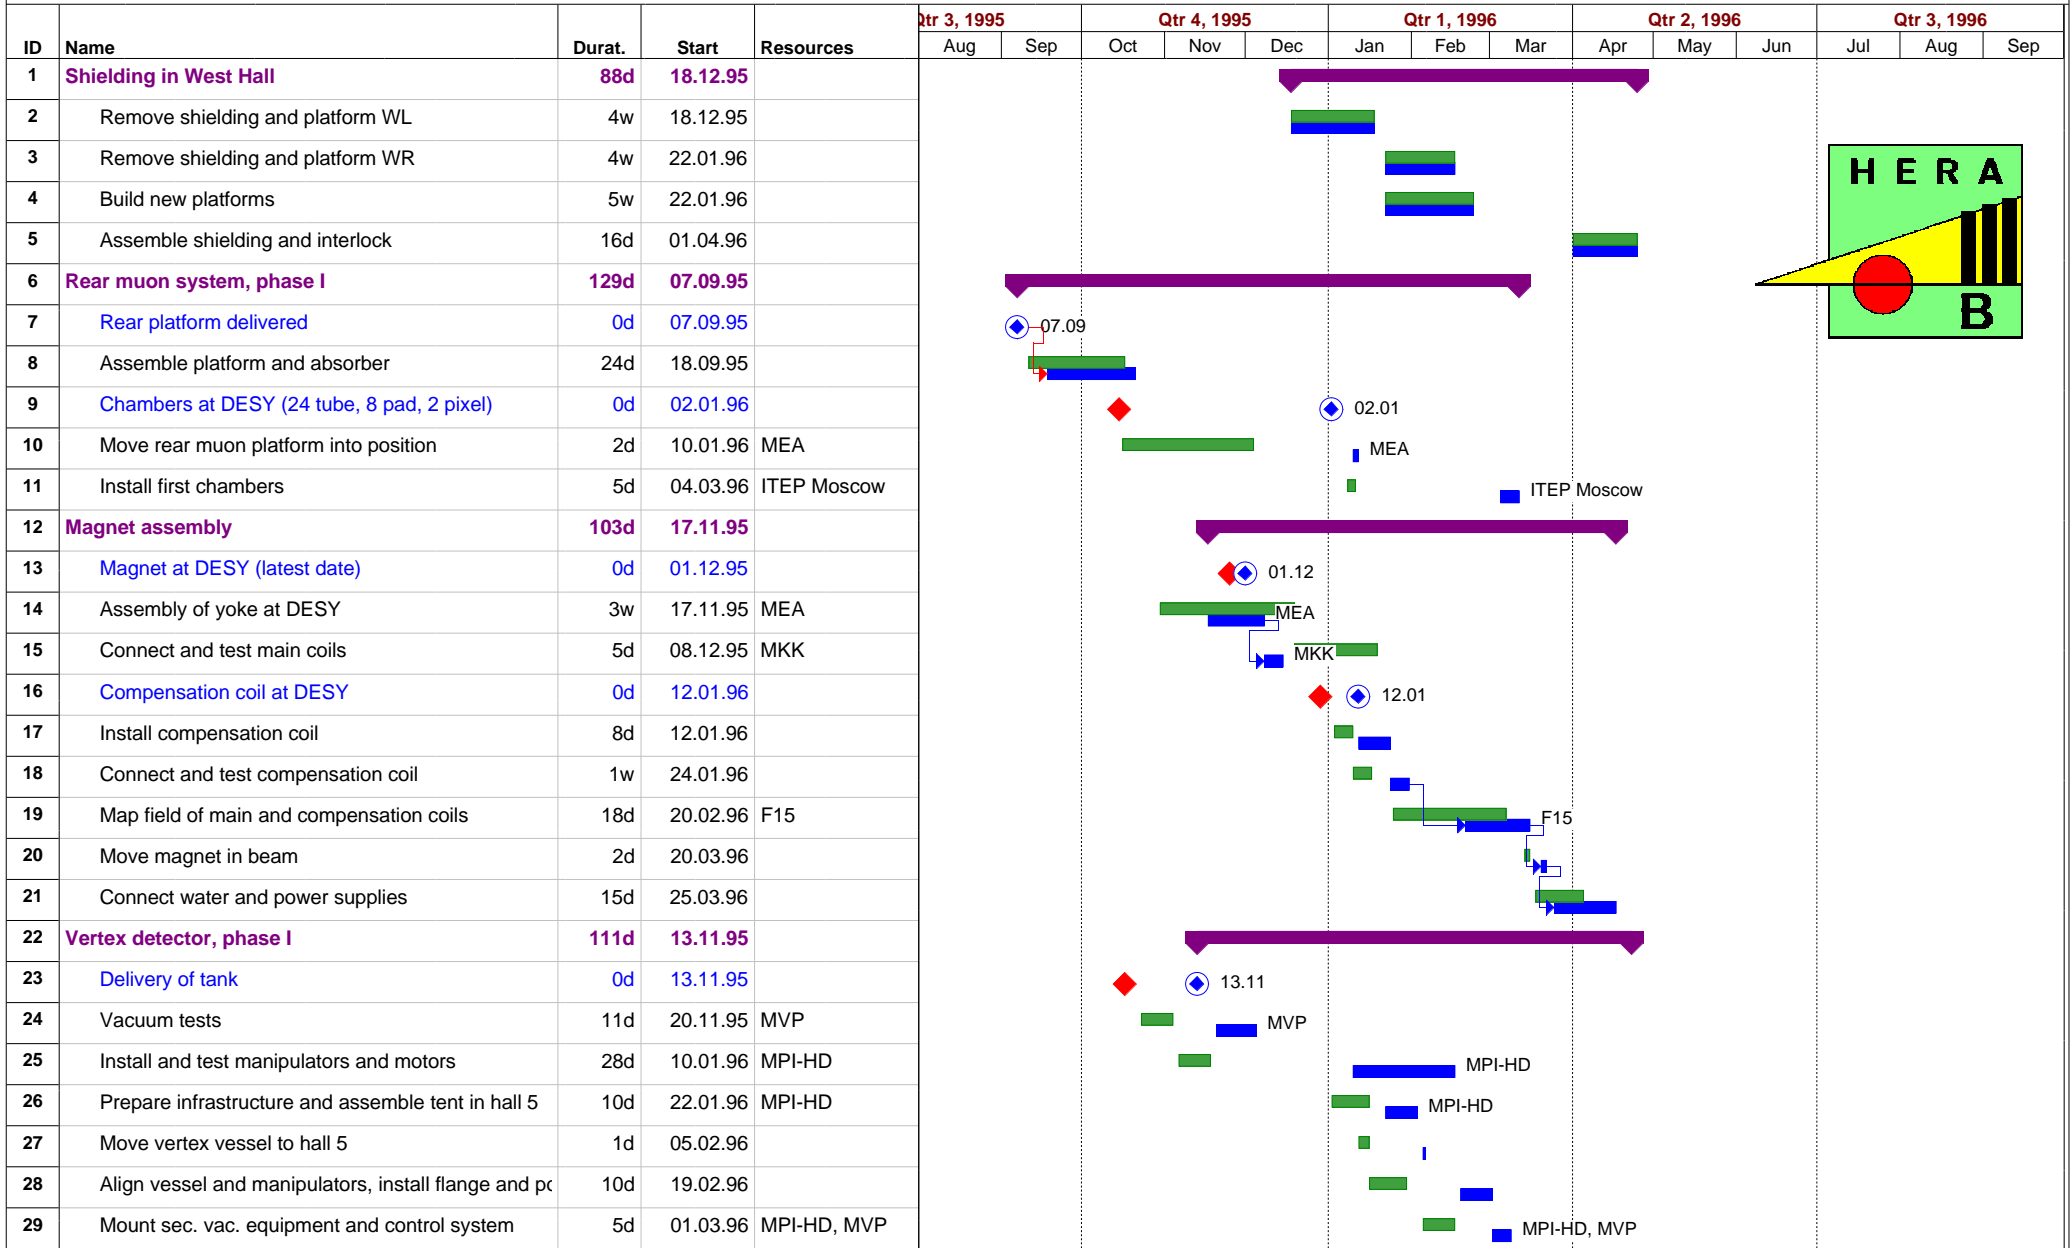

## HERA-B: Installation '96 Schedule



## HERA-B: Installation '96 Schedule

ID	Name	Durat.	Start	Resources	Qtr 3, 1995		Qtr 4, 1995			Qtr 1, 1996			Qtr 2, 1996			Qtr 3, 1996		
					Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep
30	Test vacuum control system	8d	08.03.96	MVP														
31	Assembly of window and vessel	10d	01.03.96	F15, MVP														
32	Assembly of RF shielding	1d	21.03.96	MPI-HD														
33	Mount target mechanics	2d	20.03.96	MPI-HD, Uni DO														
34	Vacuum tests	1d	25.03.96	MVP														
35	Install vertex suspension, prepare vessel installatio	2d	25.03.96	MEA														
36	Transport vessel + pipe to Hall West, attach to maç	2d	27.03.96	MEA, F15														
37	Install crane and vertex support, leak test of vessel	2d	29.03.96	MEA, MVP														
38	HERA alignment finished, move magnet in beam p	1d	03.04.96	MEA														
39	Alignment of vessel	2d	10.04.96	MEA														
40	Install and connect pumps and control system	4d	11.04.96	MVP, MPI-HD														
41	Install, test "Roman Pots" with detectors	3d	15.04.96	MPI-HD														
42	Vacuum test of complete system	3d	18.04.96	MVP														
43	Connect to HERA pipe	1d	16.04.96	MVP														
44	<b>Install prototypes</b>	<b>26d</b>	<b>15.03.96</b>															
45	Install cables	25d	15.03.96	Wille														
46	Install temporary gas distr.	4d	10.04.96	hightec														
47	Install prototype inner tracker gas system	5d	16.04.96															
48	Install prototype outer tracker gas system	5d	16.04.96															
49	Cable and test TRD prototype	5d	17.04.96															
50	Install 100 calorimeter modules	5d	10.04.96	ITEP Moscow														
51	Cable and test calorimeter	5d	17.04.96	ITEP Moscow														
52	<b>HERA TUNNEL CLOSED</b>	<b>0d</b>	<b>19.04.96</b>															
53	<b>HERA-B AREA CLOSED</b>	<b>0d</b>	<b>23.04.96</b>															

Project: Installation '96 Date: Wed 12.03.97 Page: 2	Summary		Task Progress		Critical Task Progress		Milestone		Milestone done	
	Task		Critical Task		Baseline		Baseline Milestone	
